# BRUHAT BENGALURU MAHANAGARA PALIKE

| | | |
|---|---|---|
| Clients Name | : | Executive Engineer Yelahanka Division |
| Project Name | : | Restoration and Improvements of Balance roads of AMS layout, Venugopal layout, Akashvani layout, Chikkabettahalli layout, Mahi layout and surrounding areas in ward No.03 of Yelahanka New Town Sub division(Package No.04). |
| Consultants | : | Rudraprasad Consultants |
| Project Manager /Team Leader | : | Karthik Rechan |
| Project Start Date | : | 15-Feb-22 |
| Project End Date | : | 15-Jul-22 |
| Project Length in Months | : | 6 Months |

| Sl No | Assignment | Unit | Tender Qnty | Qty of Work done | % Of Work done | Start Date | End Date | No. of Working Days |
|---|---|---|---|---|---|---|---|---|
| 1 | Removing and refixing stone slabs of drains and pointing in CM (1:3) and as per the directions of the Engineer-in-charge of the work . | Sqm | 998.57 | 1248.78 | 125 | 16-02-22 | 26-02-22 | 10 |
| 2 | Providing two line dressing to granite stone slab / granite stone masonry as per specifications. and as per the directions of the Engineer-in-charge of the work . | Sqm | 998.57 | 1491.96 | 149 | 18-02-22 | 28-02-22 | 10 |
| 3 | Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications and as per the directions of the Engineer-in-charge of the | Sqm | 8302.02 | 8620.71 | 104 | 18-02-22 | 28-02-22 | 10 |
| 4 | Providing and laying in position plain cement concrete of mix 1:4:8 with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregates @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, including cost of all materials, labour, HOM | Cum | 1387.59 | 1430.05 | 103 | 20-02-22 | 28-02-22 | 8 |
| 5 | Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal coarse aggregate at 0.69cum and fine aggregate at 0.43cum Machne mixed, well compacted for wall and Bottom including centering shuttering,cost of materials,HOM of Machinery,Curing | Cum | 2699.81 | 2608.59 | 97 | 23-02-22 | 05-03-22 | 10 |
| 6 | Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, | Tonne | 164.76 | 167.10 | 101 | 20-02-22 | 28-02-22 | 8 |
| 7 | Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing curing ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,copmplete. | Sqm | 6123.22 | 5464.43 | 89 | 03-02-22 | 13-02-22 | 10 |
| 8 | Providing and fixing RCC precast cover slab of 230mm thick for drain in cement concrete 1 1.5:3 using graded granite jelly 20mm and down size with steel reinforcement, including form work, lift charges, curing and concrete finished surfaces on both sides etc, complete and as per drawing and the directions of Engineer in-charge | Sqm | 414.18 | 155.40 | 38 | 03-03-22 | 08-03-22 | 5 |
| 9 | Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM | Cum | 159.07 | 259.21 | 163 | 13-03-22 | 18-03-22 | 5 |

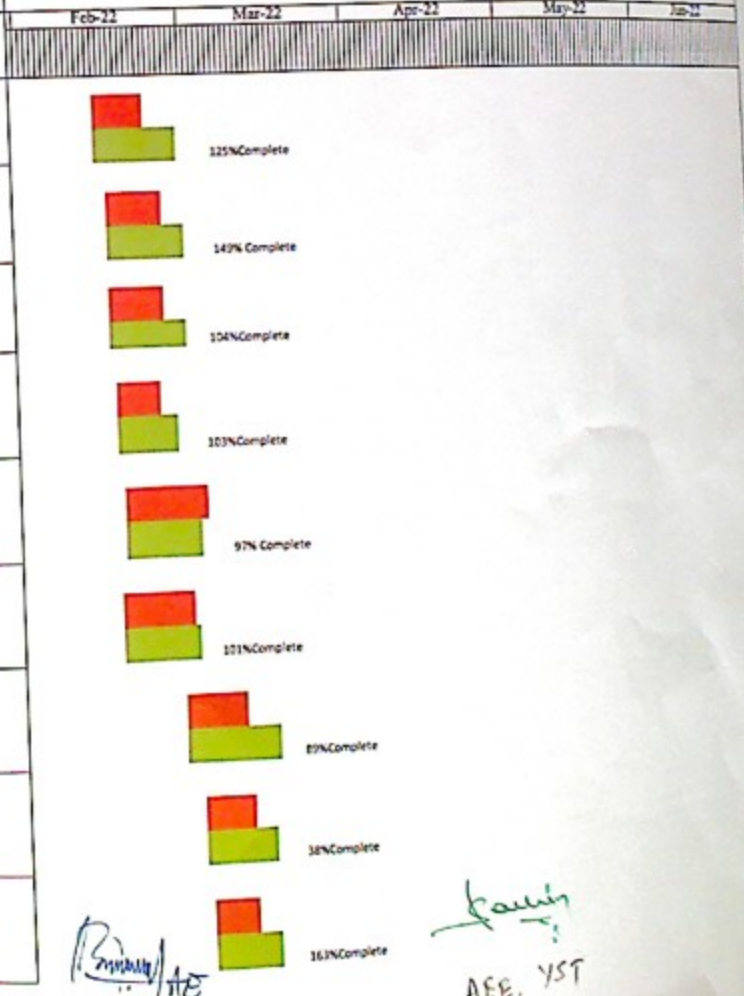


AEE, YST

# BRUHAT BENGALURU MAHANAGARA PALIKE

| | | |
|---|---|---|
| Clients Name | : | Executive Engineer Yelahanka Division |
| Project Name | : | Restoration and Improvements of Balance roads of AMS layout, Venugopal layout, Akashvani layout, Chikkabettahalli layout, Mahi layout and surrounding area in Yelahanka New Town Sub division(Package No.04). |
| Consultants | : | Rudraprasad Consultants |
| Project Manager /Team Leader | : | Karthik Rechan |
| Project Start Date | : | 15-Feb-22 |
| Project End Date | : | 15-Jul-22 |
| Project Length in Months | : | 6 Months |

| Sl No | Assignment | Unit | Tender Qnty | Qty of Work done | % Of Work done | Start Date | End Date | No. of Working Days |
|---|---|---|---|---|---|---|---|---|
| 10 | Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead and lift, transportation | m | 17675.00 | 18299.00 | 104 | 13-03-22 | 23-03-22 | 10 |
| 11 | Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications. and as per the directions of the Engineer-in-charge of the work . | Sqm | 2783.76 | 2882.08 | 104 | 07-03-22 | 13-03-22 | 6 |
| 12 | Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications and as per the directions of the Engineer-in-charge of the work . | Cum | 4809.48 | 4846.60 | 101 | 26-02-22 | 03-03-22 | 5 |
| 13 | Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications. and as per the directions of the Engineer-in-charge of the work | Sqm | 13741.38 | 13840.16 | 101 | 27-02-22 | 04-03-22 | 5 |
| 14 | Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve | Cum | 2061.21 | 2091.02 | 101 | 14-03-22 | 24-03-22 | 10 |
| 15 | Providing, laying, spreading and compacting cushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory | Cum | 2748.28 | 2788.00 | 101 | 16-03-22 | 26-03-22 | 10 |

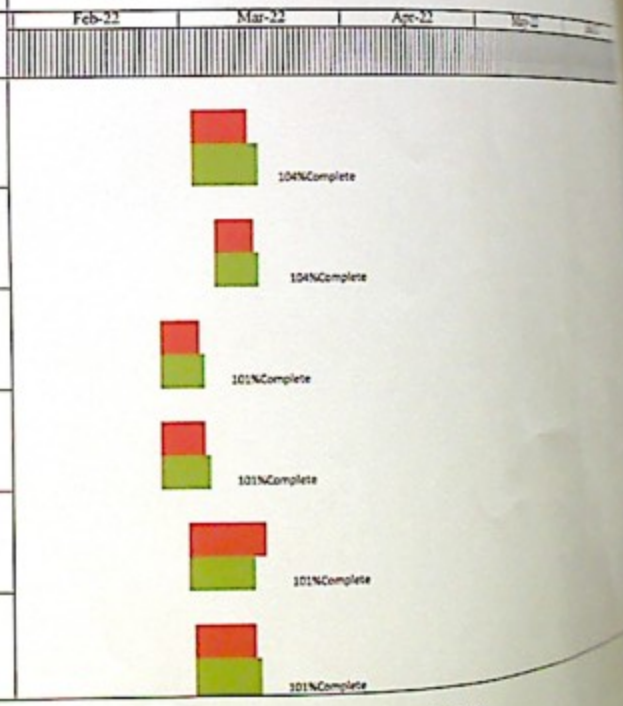


AEE, YST
